

Engineer Report for May 13, 2019

Fireman's Park Splash Pad

Weather is impacting some of the tasks necessary to complete this project. Storm sewer, filling for the path at CTH M, and preparation for the splash pad play areas is being impacted by the weather. The contractor is working on each of these tasks as the weather permits. Concrete bases and conduit continue for the lighting and work on the building also continues.

Well 6 Pumping Station Construction

The well driller has the 26-inch casing reamed and installed to a depth of 110 feet and continues to drill and install the casing pipe.

Verona Area High School

AECOM and City staff are awaiting the submittal of final plans and specifications for review and possible issuance of the erosion control and storm water permits required for this project.

CTH M Reconstruction

The roadway contractor continues to work on the bridge at the intersection of CTH M and CTH PD. As part of the roadway construction CTH M will be closed from Cross Country Road to CTH PD. A signed detour route is planned and will be implemented soon. Included with this report is a copy of the detour route that will be implemented.

The utility contractor has mobilized back to the construction site and it is expected that utility construction will begin soon.

CTH M/ Liberty Drive/ Thousand Oaks Trail Traffic Signals

The contractor started construction April 29th. Currently the sawcutting and removals are complete, preparation of subgrade has started for the widening of the roadway, some conduit and pull boxes for the new signals have been installed. The existing asphalt has yet to be milled off. The project is anticipated to be completed by June.

CTH PD - Woods Road to CTH M

A pre-bid meeting was held on May 8th for this project and the bid opening will be conducted on Wednesday May 22.

Silent Street Dredging


The dredging operation is complete. Restoration of the banks will be handled by City staff.

Meister Addition West Pond Dredging

This pond adjacent to Northern Lights Road is scheduled for significant maintenance this year. The pond was pumped down on 4/15 and 4/16 and a survey of existing conditions was completed on 4/16. A public information meeting is scheduled for May 1st. Letters to residents adjacent to the pond will be mailed out. It is anticipated that this maintenance work will be completed during a 2 week window in May, provided no weather delays.

City of Verona Standard Construction Details

AECOM has submitted standard detail drawings for final review by City staff. This includes roadway, water main, sanitary and storm sewer, and other incidental details.

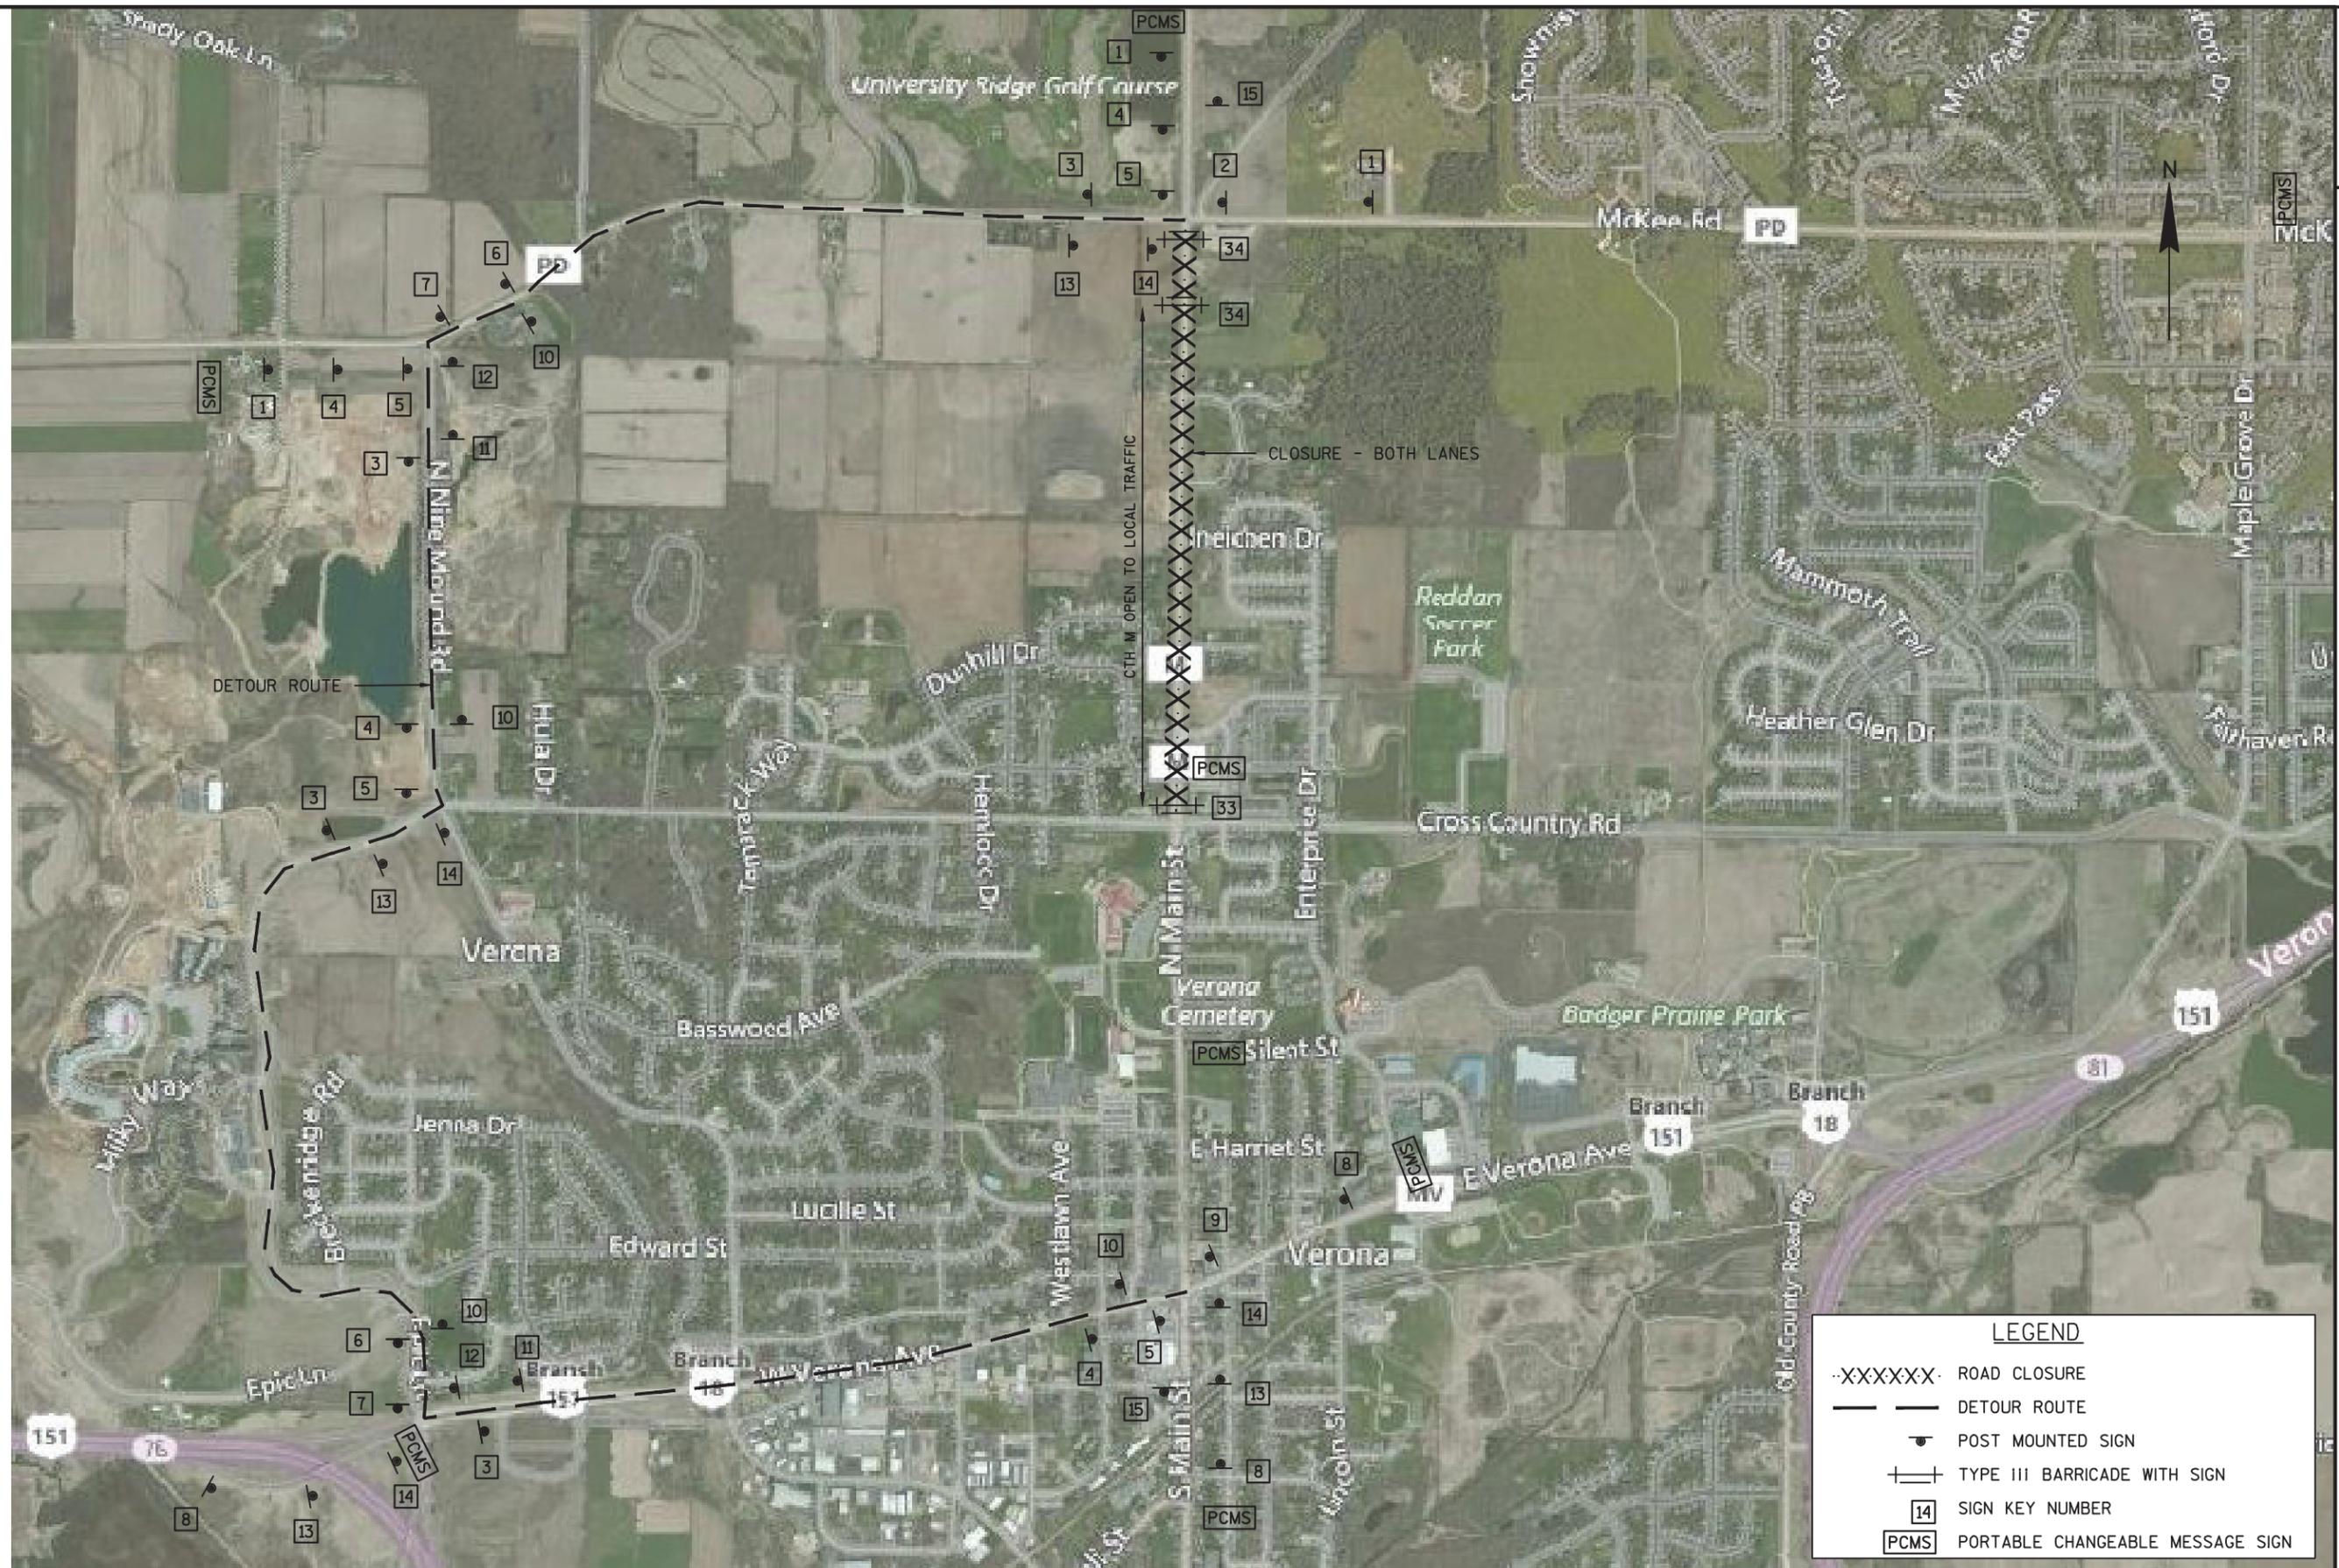

LEGEND	
·XXXXXX·	ROAD CLOSURE
---	DETOUR ROUTE
▲	POST MOUNTED SIGN
⊕	TYPE III BARRICADE WITH SIGN
14	SIGN KEY NUMBER
PCMS	PORTABLE CHANGEABLE MESSAGE SIGN
